




# SAFETY IMPROVEMENTS FOR STATE ROUTE 1

GLORIA ROBERTS  
DISTRICT DIRECTOR  
CALIFORNIA DEPARTMENT OF TRANSPORTATION — DISTRICT 7

# AREA OF INTEREST

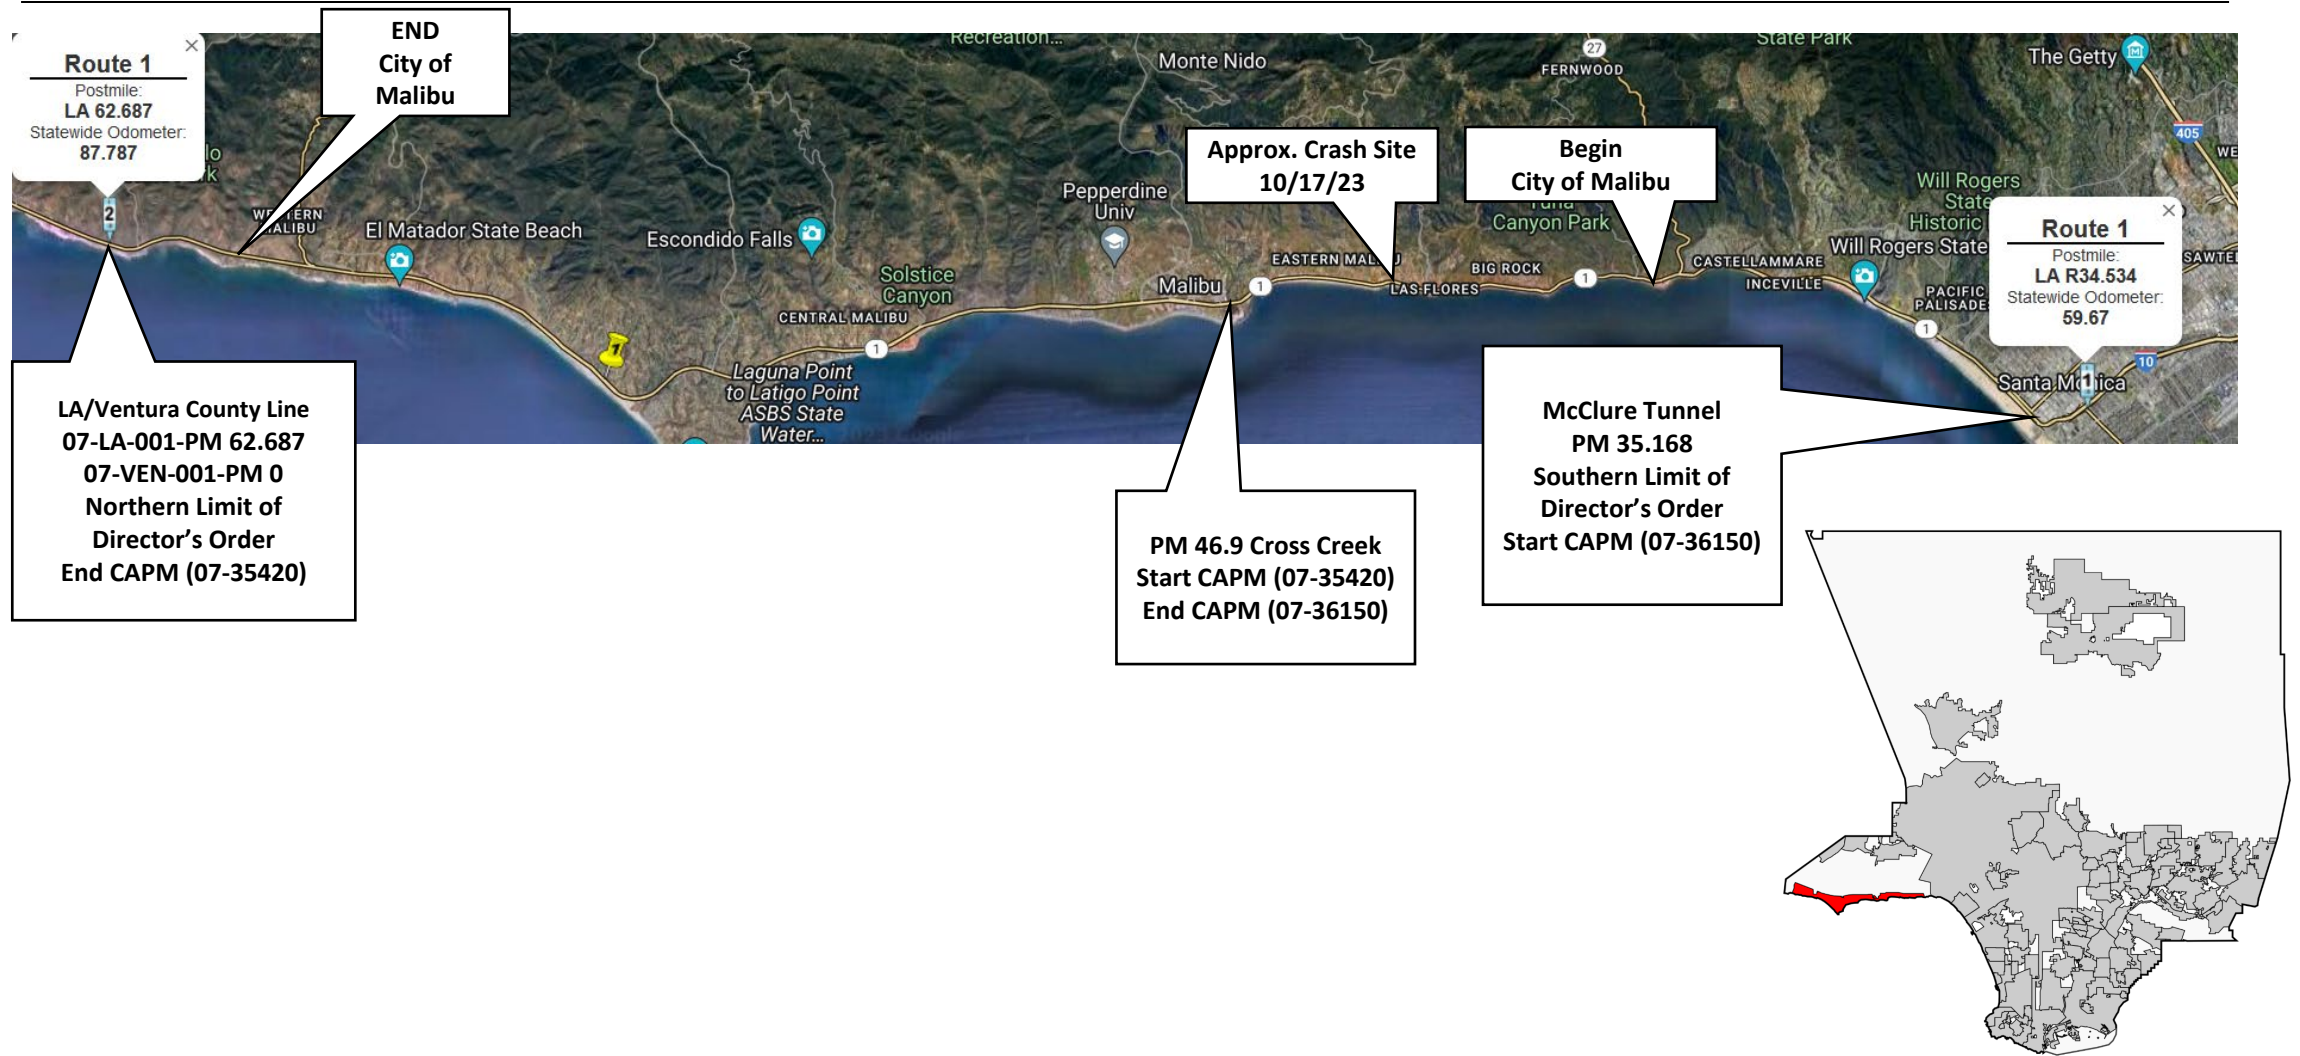




# SHORT-TERM IMPROVEMENTS



#	ITEM	DESCRIPTION	START	STATUS	ORDERED	LEADTIME
1	PORTABLE SPEED FEEDBACK TRAILERS	DEPLOY TEMPORARY PORTABLE SPEED FEEDBACK TRAILERS (10 LOCATIONS)	12/19/2023	COMPLETED		
2	PERMANENT SPEED FEEDBACK SIGNS	INSTALL PERMANENT SPEED FEEDBACK SIGNS (10 LOCATIONS)	TBD	PENDING DELIVERY OF MATERIALS	TBD	60 DAYS
3	QWICK KURB	REFLECTIVE CENTER MEDIAN SEPARATOR	1/15/2024	PENDING DELIVERY OF MATERIALS	12/28/2023	3 WEEKS
4	TEMPORARY STRIPING	REMOVE EXISTING AND INSTALL TEMPORARY STRIPING	1/8/2024	ON GOING		
5	SIGN INSTALLATION	INSTALL REGULATORY AND WARNING SIGNS AS APPROPRIATE	1/5/2024	ON GOING	12/22/2023	2 WEEKS

# SHORT-TERM IMPROVEMENTS

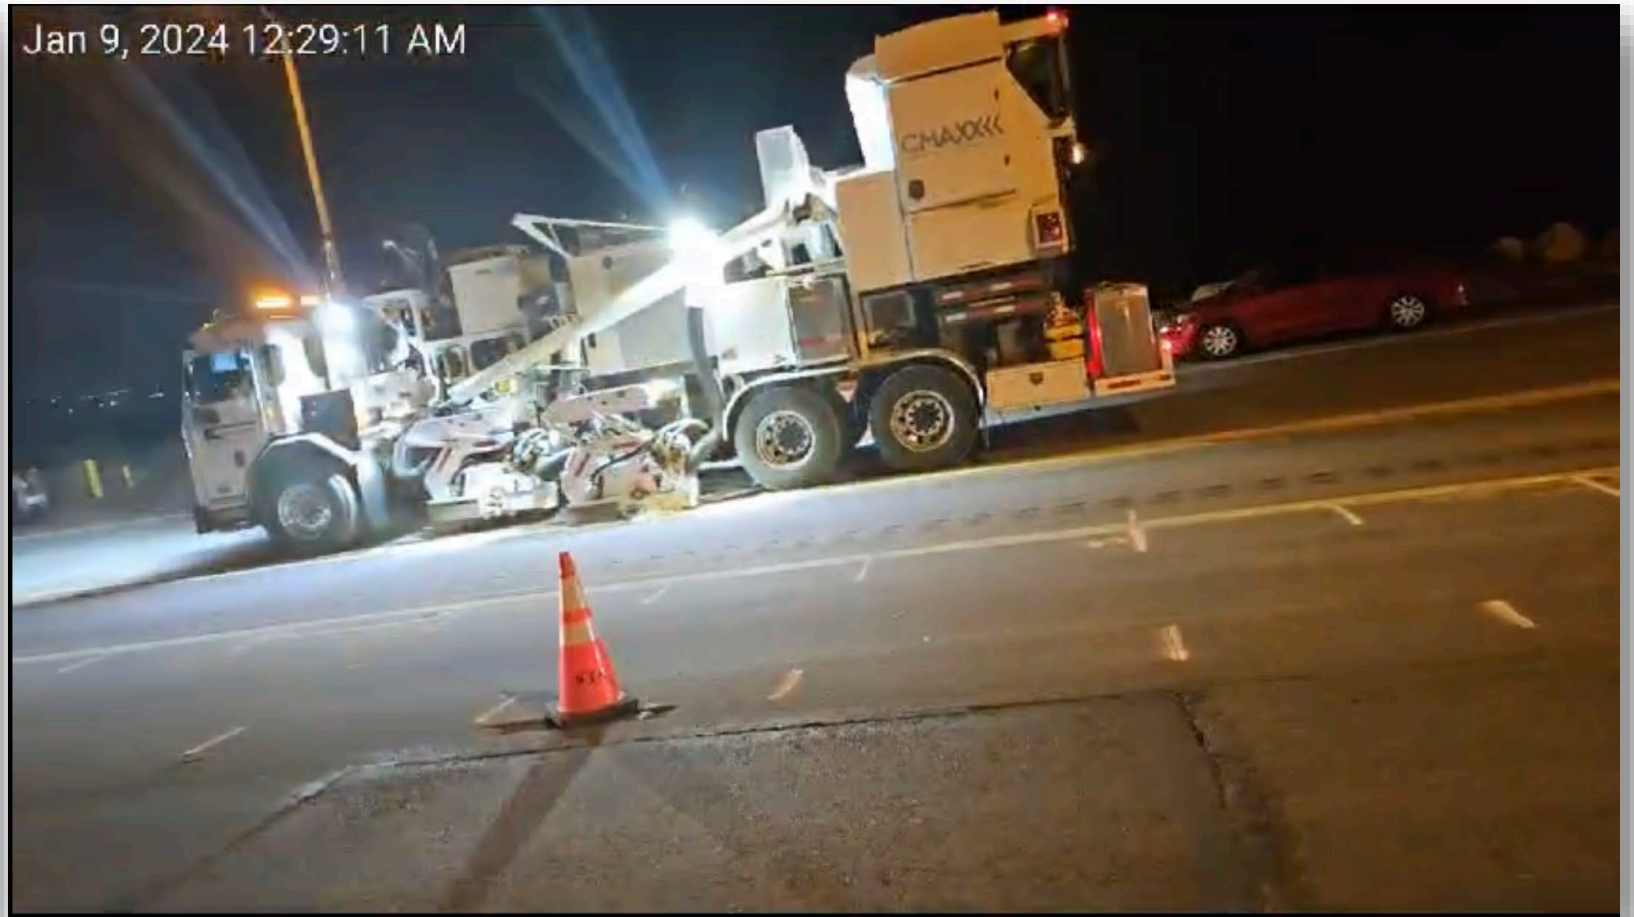

# MID- TO LONG-TERM IMPROVEMENTS



## 1. LEVERAGE UPCOMING SHOPP PROJECTS ON SR-1

- 2 CAPITAL PREVENTATIVE MAINTENANCE PROJECTS (CAPM)
- CONDUCT TWO ADDITIONAL ROAD SAFETY AUDITS
- REVISIT 2015 PACIFIC COAST HIGHWAY SAFETY STUDY

## 2. PCH MASTER PLAN

